CAPISTRANO UNIFIED SCHOOL DISTRICT San Juan Capistrano, California

March 2, 2009

TO:

Ellen Addonizio, President

and Members

Board of Trustees, Capistrano Unified School District

FROM:

Suzette Lovely, Deputy Superintendent

SUBJECT: UPDATE OF PLANS/PROGRESS OF PERFORMING ARTS THEATERS: CAPISTRANO VALLEY HIGH SCHOOL AND DANA HILLS HIGH

SCHOOL

BACKGROUND INFORMATION

In June 2008, the district began exploring concepts for two new performing arts theaters on the campuses of Dana Hills High School and Capistrano Valley High School. The need to develop these concepts came from the application and approval of the Career Technical Education (CTE) grants that were awarded in spring 2008.

On October 6, 2008, the Board authorized district staff to move into the design phase of the projects by awarding architectural contracts to prepare construction drawings of each theater and to represent the District through completion of construction. The district's design team has completed several tasks including floor plans, elevations and final renderings.

CURRENT CONSIDERATIONS

This agenda item provides an update to the Board of Trustees describing the final designs of the theaters, along with the project schedules and budget outlines, Exhibit A, Capistrano Valley High School and Exhibit B, Dana Hills High School. Exhibit C is a list of the funding sources for both Capistrano Valley High School and Dana Hills High School Performing Arts Theaters.


FINANCIAL IMPLICATIONS

This agenda item will not impact the District's General Fund. Costs associated with the preparation of theater designs will be funded from the District's developer fee account.

STAFF RECOMMENDATION

It is respectfully requested that Board President, Ellen Addonizio recognize Ron Lebs, Deputy Superintendent, who will introduce this agenda item, and will then call upon Mr. Robert Hensley of WLC Architects, Inc., who will make a brief presentation.

INFORMATION/ DISCUSSION

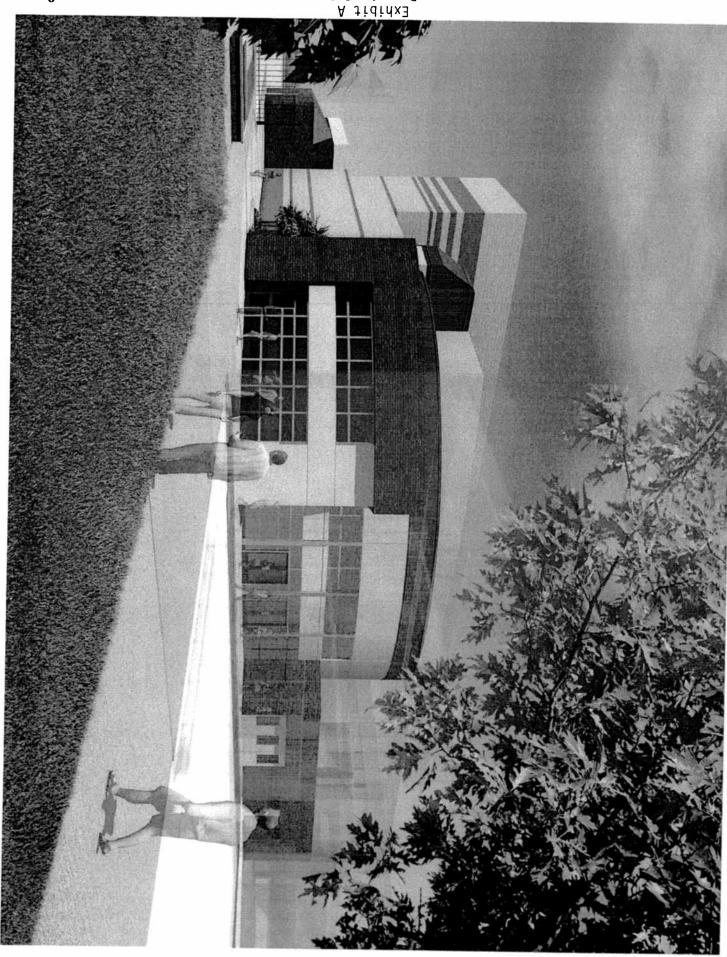

A jididxa A jo L 9gsq

PRACTICE

SCENERY SHOP

CHORAL ROOM

W

Capistrano Unified School District

Junium, 2009 First Floor Plan

ORCHESTRA EXISTING TWO STORY BUILDING BAND ROOM BLACK BOX THEATER STAIR 2 EXISTING TWO STORY BUILDING STAGE LOBBY

Exhibit A Page 2 of 6

Capistrano Unified School District



Second Floor Plan


K BLACK BOX THEATER OPENTO BELOW CAT WALK ROOF BELOW D OPEN TO BELOW BALCONY EXISTING TWO STORY BUILDING STAGE


Exhibit A Page 3 of 6





















CAPISTRANO UNIFIED SCHOOL DISTRICT

CAPISTRANO VALLEY HIGH SCHOOL

PERFORMING ARTS FACILITY - EXHIBIT "A"

			December 8, 2008			
				%	B	Sudgeted Amount for DSA
A	. ESTIMATED CONSTRUCTION (HARD) COSTS	<u> </u>	Budgeted Amount	Compl	ete	Approval & Bidding
	·					
1	New Building Construction	\$	6,717,075			
2	Existing Building Modifications	\$	91,000			
3	Sustainable Architecture	\$	403,025			
4	Remodel of Existing Buildings	\$	100,023			
5	General Site Development	\$	235,000			
6	Subtotal:	\$	7,446,100	0%	\$	
7	Demo / Removal Building & Site	\$	48,000	070	4	•
8	Wet Utilities (Water, Sewer, Drainage, Fire) Upgrades	\$	73,000			
9	Dry Utilities (Electrical, Low Voltage) Upgrades	\$	135,000			
10	Site Clean-Up (DTSC/HAZMAT)	\$	50,000			
11	Subtotal:	3	306,000	0%	\$	
12	Available for Construction (Prime Contractor Bids)	\$	7,752,100	0%	\$	•
13	Construction Estimate Contingency	\$	387,605	0.70	•	•
14	Subtotal:	\$	8,139,705	0%		
15	CM's or GC's General Conditions Costs	\$	465,126	U76	\$	-
16	Subtotal:	\$	8,604,831	~~		
17	CM's or CG's Fees	•	\$498,361	0%	\$	•
18	BID CONTINGENCY (Escalation)	\$				
		4	546,192			
19	TOTAL EST. CONSTRUCTION COST:	3	9,649,384	ΛW		
			7,047,304	0%	\$	•
B. 20 21 22	Site Surveys / Topos Site Geotech / Soil Borings	\$ \$	25,974 23,395	100% 100%	\$	25,974 23,395
Eutopologica	Fumiture, Fixtures, Equipment (FFE) Allowance	\$	400,000	0%	\$	-
23	Architect/Engineer Fees	\$	768,631	80%	\$	614,905
24	Specialty Consultants				100000	
	a. Acoustical Engineer	\$	36,150	80%	\$	28,920
25	b. Theatre Engineer DSA Plancheck Fees	\$	147,300	80%	\$	117,840
26		\$	53,512	100%	\$	53,512
27	CDE Project Review Fees	\$	6,755	100%	\$	6,755
	DTSC/HAZMAT Environmental Consultant/Fees CEQA Consultant	\$	33,773	100%	\$	33,773
29		5	54,641	100%	\$	54,641
30	Utility City/County Fees & Inspections	\$	100,000	50%	15	50,000
31	DSA Inspector of Record	\$	144,741	0%	\$	-
	Special Inspection + Materials Testing	\$	48,247	0%	\$	
32	Labor Compliance Program Administration	\$	~	0%	\$	
33 34	Bidding / Reimbursable	\$	58,141	75%	\$	43,606
	Subtotal:	\$	1,901,259	0%	\$	1,053,320
35	PROJECT CONTINGENCY (District reserve added cost)	\$	434,222	10%	\$	43,422
36 37	TOTAL ESTIMATED SOFT COST:	\$	2,335,482	47%	\$	1,696,742
38	TOTAL ESTIMATED PROJECT BUDGET:	\$	11,984,866	9%	\$	1,096,742
39	SOFT COST (School Board Approved to Date)	\$	823,272	81%	\$	669,546
40	SOFT COST (School Board to Review for Consideration on Dece	ember 8, 200	8)		5	427,197
1	PREPARED BY ARCHITECT:	APPROVE	D BY DISTRICT:			
	/					
4	(Χ				
	Exhibi					
	Page 5	of 6				

January 12, 2009

Performing Arts Theater - Capistrano Valley High School PROJECT TIMELINE A - Construction Start: December 2009

Capistrano Unified School District

San Juan Capistrano, CA

WLC Architects, Inc. 08-140.02

PHASE: DESCRIPTION	Duration Days	Star Date	
0.0 Programming		May 19, 2008	Complete
0.01 General Topographic Aerial Mapping		May 19, 2008	Complete
0.1 District Review	65	September 1, 2008	November 5, 2008
0.11 Facilities Sub Committee	1	September 16, 2008	September 17, 2008
0.12 Board Presentation/ Approval	1	October 6, 2008	October 7, 2008
0.13 Contracts	30	October 7, 2008	November 6, 2008
1.0 Schematic Design	55	November 7, 2008	January 1, 2009
1.1 Detail Topographic / Boundary Survey	30	November 4, 2008	December 4, 2008
1.2 Geo-technical Investigation	30	December 8, 2008	January 7, 2009
1.3 Board Presentation	1	January 12, 2008	January 13, 2008
2.0 Design Development	45	January 2, 2009	February 16, 2009
2.1 Board Presentation	1	February 16, 2009	February 17, 2009
3.0 Construction Drawings	100	February 18, 2009	May 28, 2009
3.1 DSA review	160	May 29, 2009	November 5, 2009
3.2 Board Presentation	1	June 8, 2008	June 9, 2008
3.2 DSA comments/ Back check and Approval	30	November 5, 2009	December 5, 2009
3.3 State Allocation Board	1		December 9, 2009
4.0 Bidding and Contract Negotiations	45	December 14, 2009	January 28, 2010
4.1 Contract Negotiation	30	January 28, 2010	February 27, 2010
4.2 Board Approval (estimated date) / Notice to Proceed	10	March 9, 2010	March 19, 2010
5.0 Construction	540	March 19, 2010	September 10, 2011
Total Project Timeline	ibit A	May 19, 2008	September 10, 2011

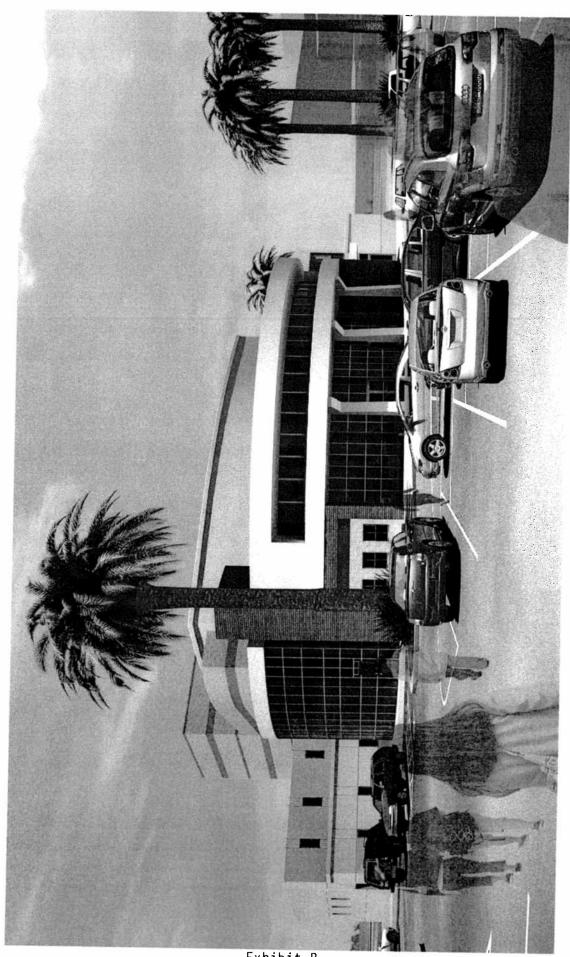


Exhibit B Page 1 of 6

Capistrano Unified School Instruct

March Commango UMC;
1913 Andrew (Person
1914) Andrew (Person
1915)
Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andrew (Person
1915) Andre



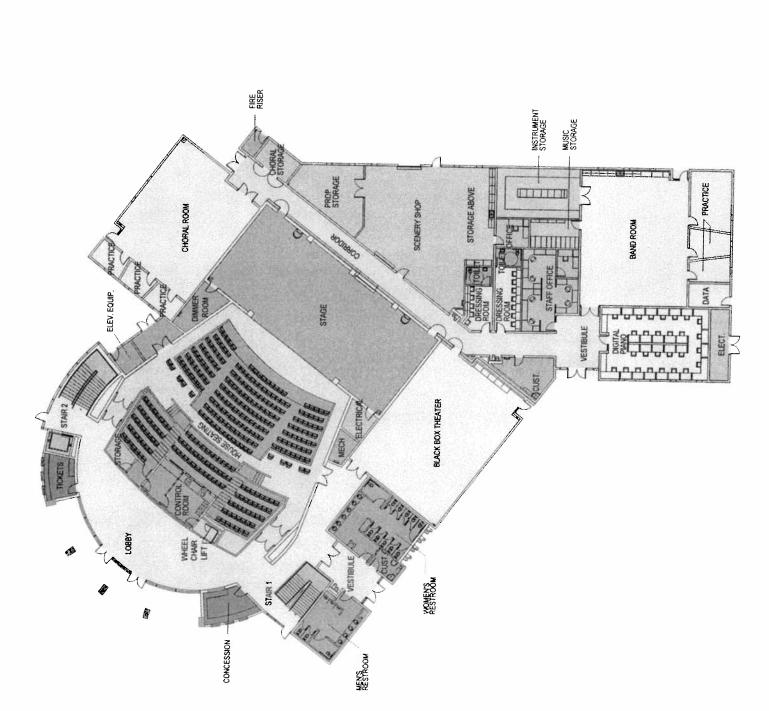


Exhibit B Page 2 of 6

Capistrano Unified School District



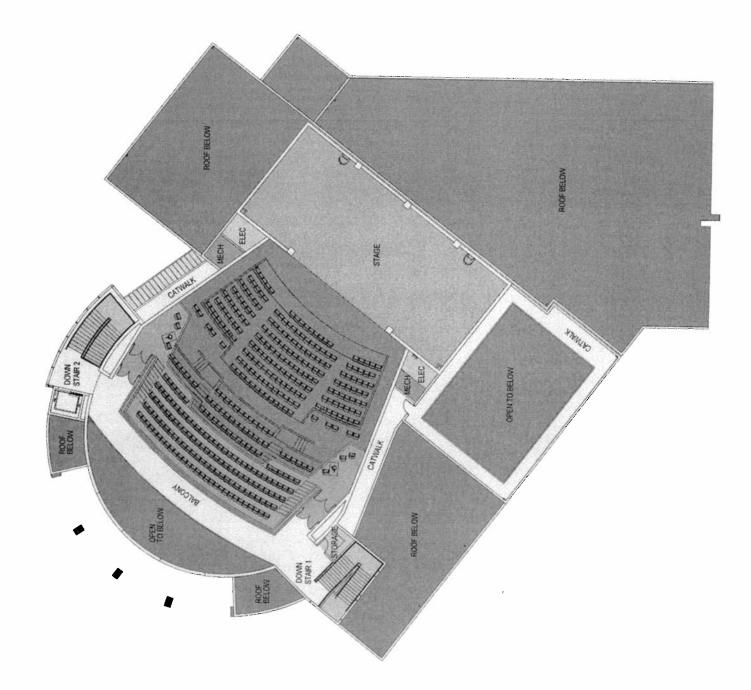


Exhibit B Page 3 of 6

Dana Hills H.S.
Performing Arts
Center



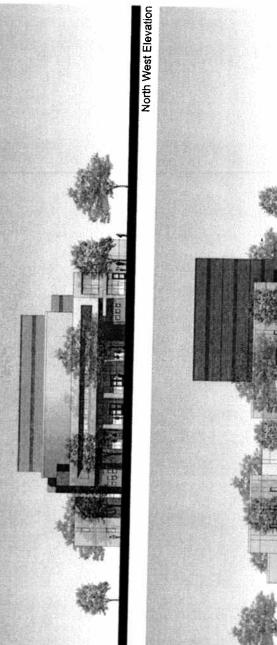







Architects, Inc.

South West Elevation

Exhibit B Page 4 of 6



CAPISTRANO UNIFIED SCHOOL DISTRICT

DANA HILLS HIGH SCHOOL PERFORMING ARTS FACILITY - EXHIBIT "A"

		December 8, 2008		·-··	
			%	В	ludgeted Amount for DSA
A. ESTIMATED CONSTRUCTION (HARD) COSTS	L	Budgeted Amount	Comp	ete	Approval & Bidding
·					
New Building Construction	\$	6,799,924			
2 Sustainable Design Features	\$	509,994			
3 New Tennis Courts & Lighting	\$	365,000			
4 Remodel of Existing Buildings	\$,			
5 General Site Development	\$	225,000			
6 Subtotal:	\$	7,899,918	0%	\$	
7 Demo / Removal Buildings / Handball Courts / Tennis Courts	s \$	162,000	0,0	•	-
8 Wet Utilities (Water, Sewer, Drainage, Fire) Upgrades	\$	88,000			
9 Dry Utilifies (Electrical, Low Voltage) Upgrades	\$	125,000			
10 Site Clean-Up (DTSC/HAZMAT)	\$	50,000			
11 Subtotal:	\$	425,000	0%	\$	
12 Available for Construction (Prime Contractor Bids)	\$	8,324,918	0%	\$	-
13 Construction Estimate Contingency	\$	416,246	O A	4	•
14 Subtotal:	\$	8,741,164	000		
15 CM's or GC's General Conditions Costs	\$	499,495	0%	\$	•
16 Subtotal:	<u>*</u>				
17 CM's or CG's Fees	\$	9,240,659 528,721	0%	\$	-
18 BID CONTINGENCY (Escalation)	\$				
	<u>\$</u>	586,163			
19 TOTAL EST. CONSTRUCTION COST:	\$	10 och Fra			
	[4	10,355,543	0%	\$	-
 B. ESTIMATED PROJECT (SOFT) COSTS 20 Site Surveys / Topos 21 Site Geotech / Soil Borings 22 Furniture, Fixtures, Equipment (FFE) Allowance 	\$ \$ \$	25,926 24,318	100%	\$	25,926 24,318
23 Architect/Engineer Fees	5	400,000	0%	\$	•
24 Specialty Consultants		801,918	80%	5	641,535
a. Acoustical Engineer	œ	0.1.77			
b. Theatre Engineer	\$	36,150	80%	\$	28,920
25 DSA Plancheck Fees	\$	147,300	80%	\$	117,840
26 CDE Project Review Fees	\$	57,113	100%	\$	57,113
27 DTSC/HAZMAT Environmental Consultant/Fees	\$	7,249	100%	\$	7,249
28 CEQA Consultant	\$	36,244	100%	\$	36,244
29 Utility City/County Fees & Inspections	5	53,081	100%	\$	53,081
30 DSA Inspector of Record	\$	100,000	50%	\$	50,000
31 Special Inspection + Materials Testing	\$	155,333	0%	\$	+
32 Labor Compliance Program Administration	\$	51 <i>,77</i> 8	0%	\$	
33 Bidding / Reimbursable	\$	-	0%	\$	*
34 Subtotal:	\$	83,249	75%	\$	62,437
35 PROJECT CONTINGENCY	\$	1,979,660	0%	\$	1,104,663
35 TROJECT CONTINGENCY	\$\$	465,999	10%	\$	46,600
TOTAL ESTIMATED SOFT COST:	\$	2,445,659	47%	\$	1,151,263
TOTAL ESTIMATED PROJECT BUDGET:	\$	12,801,202	9%	\$	1,151,263
9 SOFT COST (School Board Approved to Date)	5	854,999	81%	•	to con
10 SOFT COST (School Board to Review for Consideration on Dece	ember 8, 200		J. A.	3	6 94,616
PREPARED BY ARCHITECT:	APPROVED	BY DISTRICT:			
	VALKOVE	OF DISTRICT:			
X	Х				
Exhib					
Dago E	-E C				

January 12, 2009

Performing Arts Theater - Dana Hills High School PROJECT TIMELINE A - Construction Start: December 2009

Capistrano Unified School District


San Juan Capistrano, CA

WLC Architects, Inc.

08-138.02

PHASE: DESCRIPTION	Duration Days	Star Date	
0.0 Programming		May 19, 2008	
0.01 General Topographic Aerial Mapping		May 19, 2008	
0.1 District Review	65	September 1, 2008	
0.11 Facilities Sub Committee	1	September 16, 2008	
0.12 Board Presentation/ Approval	1	October 6, 2008	
0.13 Contracts	30	October 7, 2008	
1.0 Schematic Design	55	November 7, 2008	
1.1 Detail Topographic / Boundary Survey	30	November 4, 2008	December 4, 200
1.2 Geo-technical Investigation	30	December 8, 2008	January 7, 200
1.3 Board Presentation	1	January 12, 2008	January 13, 200
2.0 Design Development	45	January 2, 2009	February 16, 200
2.1 Board Presentation	1	February 16, 2009	February 17, 2009
3.0 Construction Drawings	100	February 18, 2009	May 28, 2009
3.1 DSA review	160	May 29, 2009	November 5, 2009
3.2 Board Presentation	1	June 8, 2008	June 9, 2008
3.2 DSA comments/ Back check and Approval	30	November 5, 2009	December 5, 2009
3.3 State Allocation Board	J		December 9, 2009
.0 Bidding and Contract Negotiations	45	December 14, 2009	
4.1 Contract Negotiation	30		January 28, 2010
4.2 Board Approval (estimated date) / Notice to Proceed		January 28, 2010	February 27, 2010
0 Construction	10	March 9, 2010	March 19, 2010
otal Project Timeline	540	March 19, 2010	September 10, 2011

Theatre Funding Sources
DHHS and CVHS
As of 12/31/2008

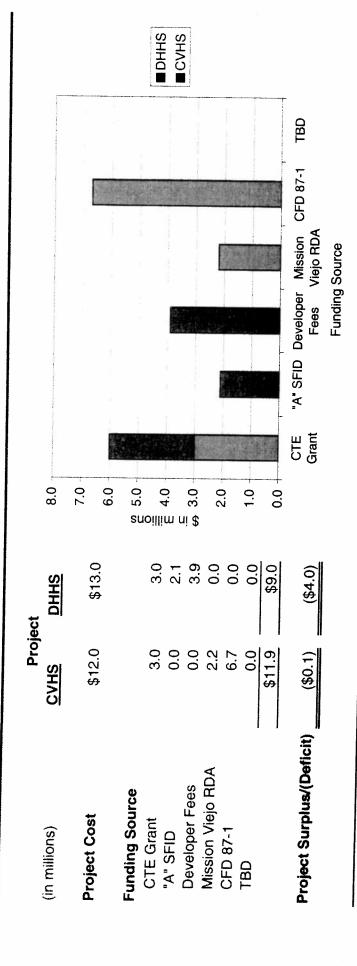

Funding Source Balances

	CTE Grant	•	"A" SFID Developer Fees MV RDA CFD 87-1	s MV RDA	CFD 87-1
Beginnnig Balance	6,000,000	6,000,000	6,000,000 6,000,000 5,168,000 2,458,000 6,733,000	2,458,000	6,733,000
Commitments					
· CVHS	3,000,000	•	•	2,200,000	6.700.000
- DHHS	3,000,000	2,100,000	3,900,000	•	
Subtotal	6,000,000	2,100,000	3,900,000	2,200,000	6,700,000
Ending Balance	6	3,900,000	3,900,000 1,268,000	258,000	33,000
